DIRIYAH DG1
LAND SURVEYING SERVICES

Project Owner : Diriyah Company

Kick-off Meeting

Task Order No. 4500009743



Consultant

Al Qotr Professional Consulting Company


Content

- Introduction
- Detailed scope of work
- Methodology
- Deliverables and reporting
- Resource deployment
- Schedule for work completion
- HSE and Welfare Measures for the workmen during the Works

Introduction

The objective of this Task Order is to provide Diriyah Company with responsive and reliable land surveying support for its minor works in the DG1 area, Riyadh.


The services cover the issuance of new title deeds (Main, Phase, Sub-Phase and Block), title deeds for plots and units, land survey and land demarcation, each instructed as an individual Minor Work Task.

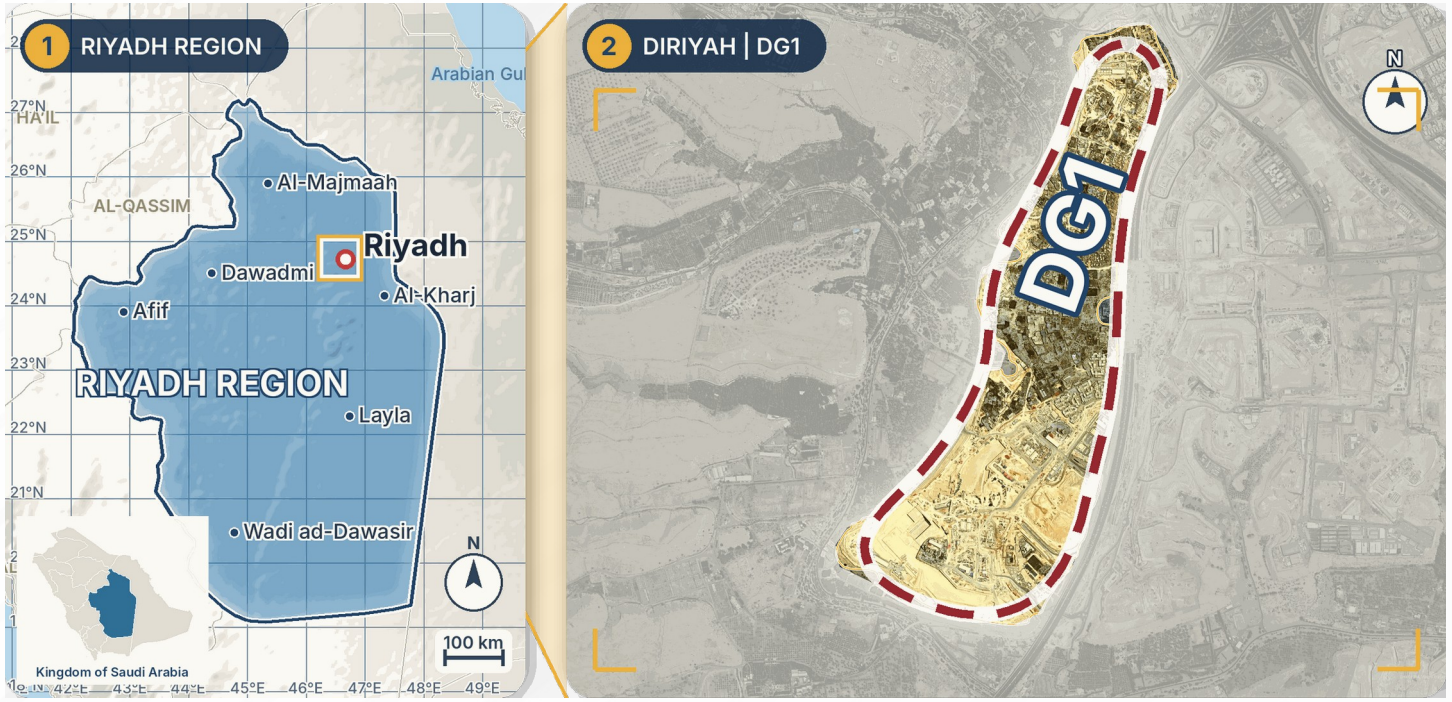

Satellite views: Riyadh Region (NASA Blue Marble) and DG1 with its surroundings (Esri). DG1 extent indicative.

Client	Diriyah Company
Task Order	No. 4500009743
Place	DG1 area, Riyadh
Start	11 October 2026
Completion	09 November 2029

Introduction

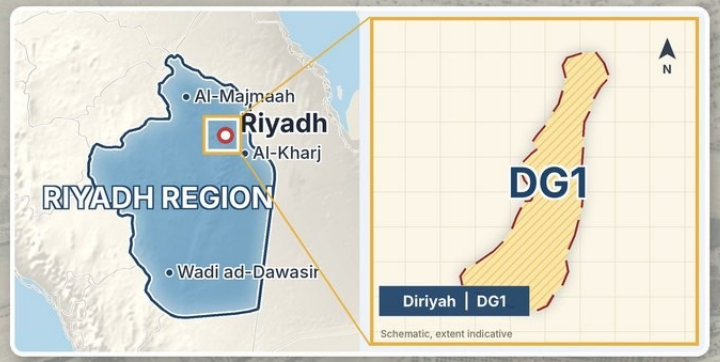

Riyadh Region, Kingdom of Saudi Arabia

Task Order details	
Client	Diriyah Company
Task Order	No. 4500009743
Service	Land Surveying, Minor Works
Place	DG1 area, Riyadh
Period	11 Oct 2026 - 09 Nov 2029

DIRIYAH DG1

Land Surveying Services - Minor Works

DG1 extent (indicative)

Zoom area (magnified x2)

Imagery: Esri. DG1 extent is indicative, pending the official boundary. Not to scale.

Methodology

Programme stages of each Task Order

Phase 1:
Initiation and Planning:

- Task Order received.
- Programme agreed.
- Team mobilized.

Phase 2:
Field Survey:

- Survey control, land and boundary survey, demarcation where instructed.

Phase 3:
Processing and Deliverables

- Field data processed; drawings and title deed documentation prepared.

Phase 4:
QA/QC and Close-Out


- QA/QC, submission, comments, authority approval if applicable, close-out.

Methodology

Quality control of survey outputs:

Descriptive data	Deed data	CAD drawing
Boundaries	Deed number	Coordinates
Lengths	Owner	Numbering
Area	ID number	Layout

Quality control at every step

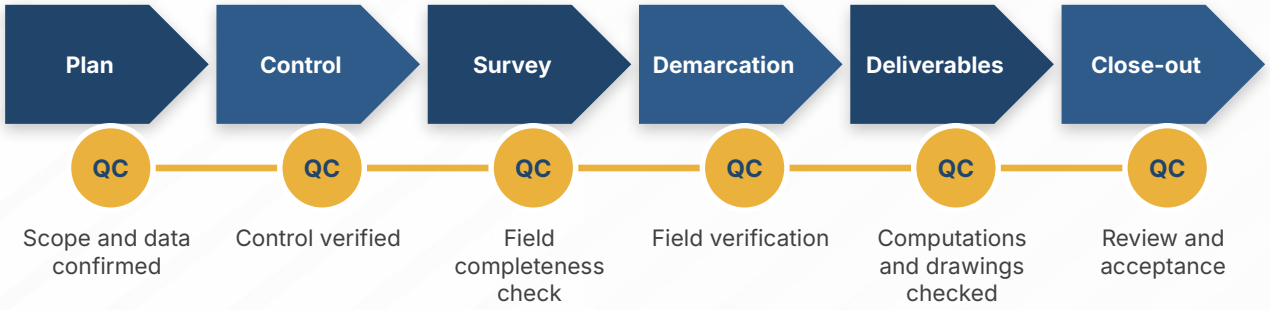


Checks run during every step, not only at the end.

Field data QC record

	X	Y	H	RMS	PDOP	Antenna Height	Survey Time
1	2738789.524	656952.3912	663.8285	0.011398	1.194	1.8	5
2	2737692.575	657783.8904	640.5952	0.011392	1.274	1.8	5
3	2737685.966	657787.694	640.4935	0.011439	1.291	1.8	5
4	2737680.463	657790.5711	640.4323	0.011469	1.291	1.8	5
5	2737673.492	657794.1414	640.3668	0.011501	1.291	1.8	5
6	2737666.545	657797.7108	640.2839	0.011345	1.291	1.8	5
7	2737661.802	657800.0192	640.2722	0.011495	1.29	1.8	5
8	2737657.479	657799.4479	640.3162	0.011491	1.326	1.8	5
9	2737658.774	657801.7611	640.1539	0.011394	1.266	1.8	5
10	2737651.462	657805.4873	640.15	0.011337	1.29	1.8	5
11	2737649.994	657803.3019	640.2545	0.011364	1.29	1.8	5
12	2737640.526	657808.114	640.2377	0.011659	1.377	1.8	5
13	2737641.481	657810.6082	640.121	0.01141	1.324	1.8	5
14	2737634.613	657814.1218	640.1142	0.011342	1.289	1.8	5
15	2737633.153	657811.9322	640.2301	0.011357	1.289	1.8	5
16	2737628.346	657814.4081	640.2547	0.012109	1.289	1.8	5
17	2737626.18	657818.3519	640.1623	0.011455	1.289	1.8	5

Sample QC table from previous Alqotr work

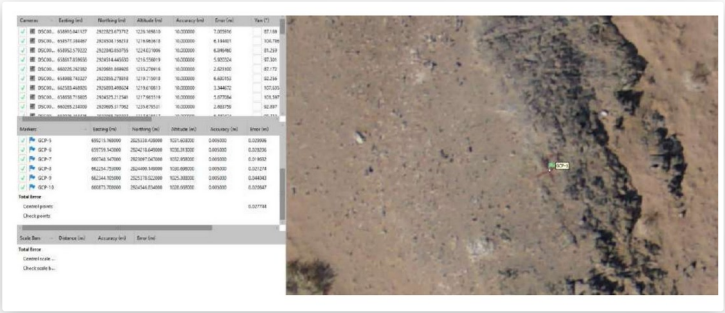

Control point check: sample from the Alqotr quality guide

Methodology

Survey :

Survey control

- Survey control is verified or established where required, before any field survey starts.

Land and boundary survey

- Field data is acquired for the instructed land, based on the available approved information.

Field verification

- Completeness checks are made in the field before data processing.




Methodology

Land Demarcation:

Land demarcation is carried out where instructed in the Task Order.


- ❑ Verify survey control points and benchmarks
- ❑ Stake out plot corners with Total Station or RTK GNSS
- ❑ Fix boundary markers and reference them with IDs
- ❑ Photograph each corner and marker
- ❑ Cross-check with the available approved information
- ❑ Corner coordinates
- ❑ Marker IDs
- ❑ Photo record
- ❑ Demarcation report

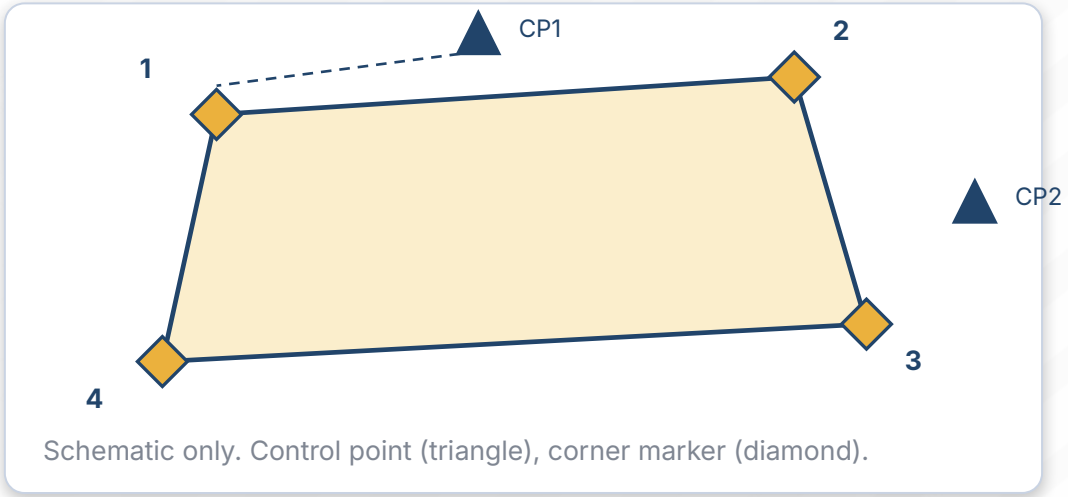

Schematic only. Control point (triangle), corner marker (diamond).





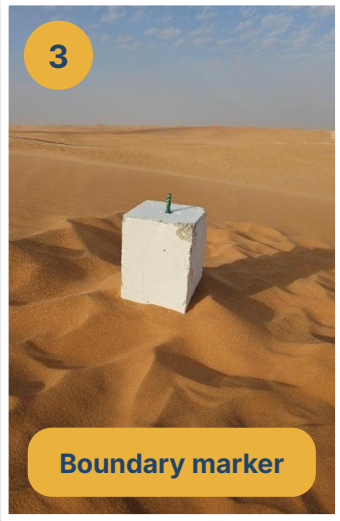

Methodology

Workflow and schedule:

Task Order period: 11 Oct 2026 to 09 Nov 2029

Approval before work starts: 6 working days

1 Plan	2 Control	3 Survey	4 Demarcation	5 Deliverables	6 Close-out
Task Order, programme	Verify survey control	Land and boundary survey	Stake-out and markers	Processing, drawings, QA/QC	Review, approval, final submission




Milestones

1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10

M1 Receipt | M2 Programme agreed | M3 Mobilized | M4 Field survey done | M5 Draft ready | M6 QA/QC done | M7 Submitted | M8 Comments closed | M9 Final submission | M10 Close-out

Deliverables

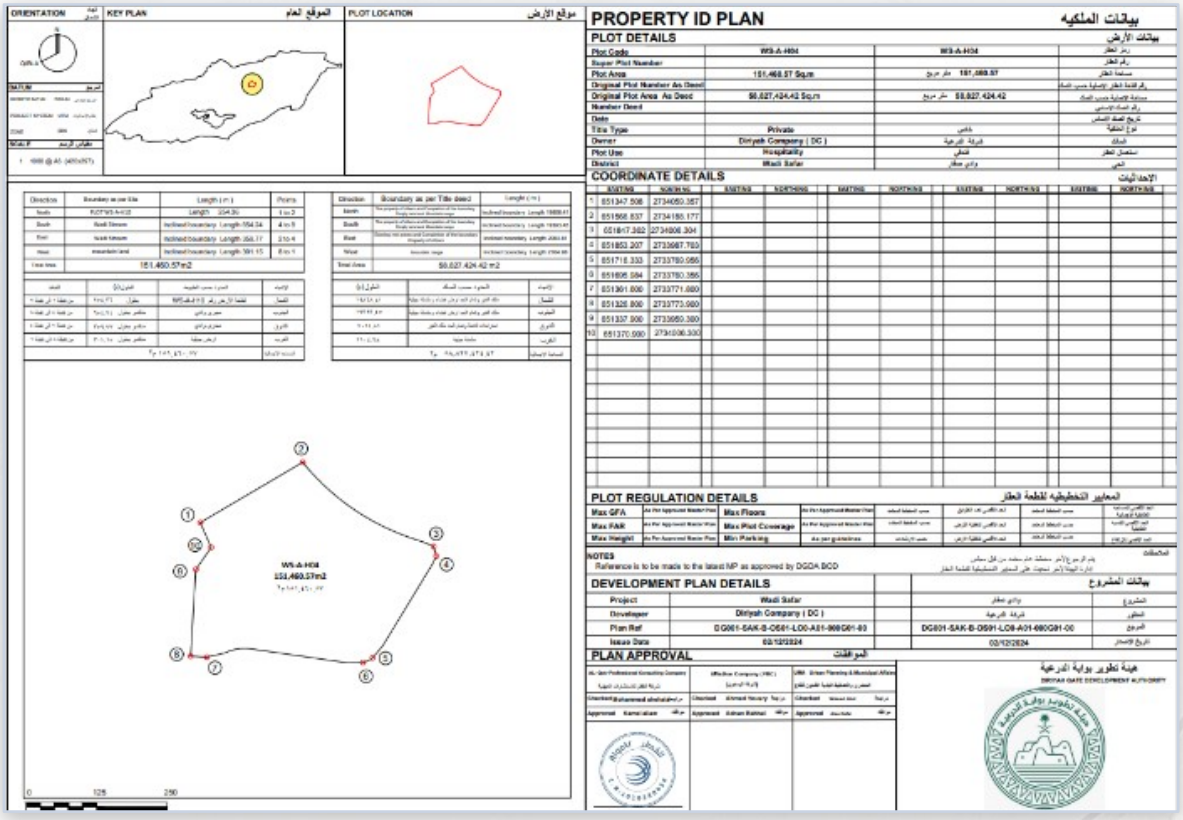

Survey decision (Property ID Plan): sample from previous Alqotr work



Plot photo record: sample from previous Alqotr work


Survey drawings

Title deed documents

Demarcation report

Final survey records

Resource

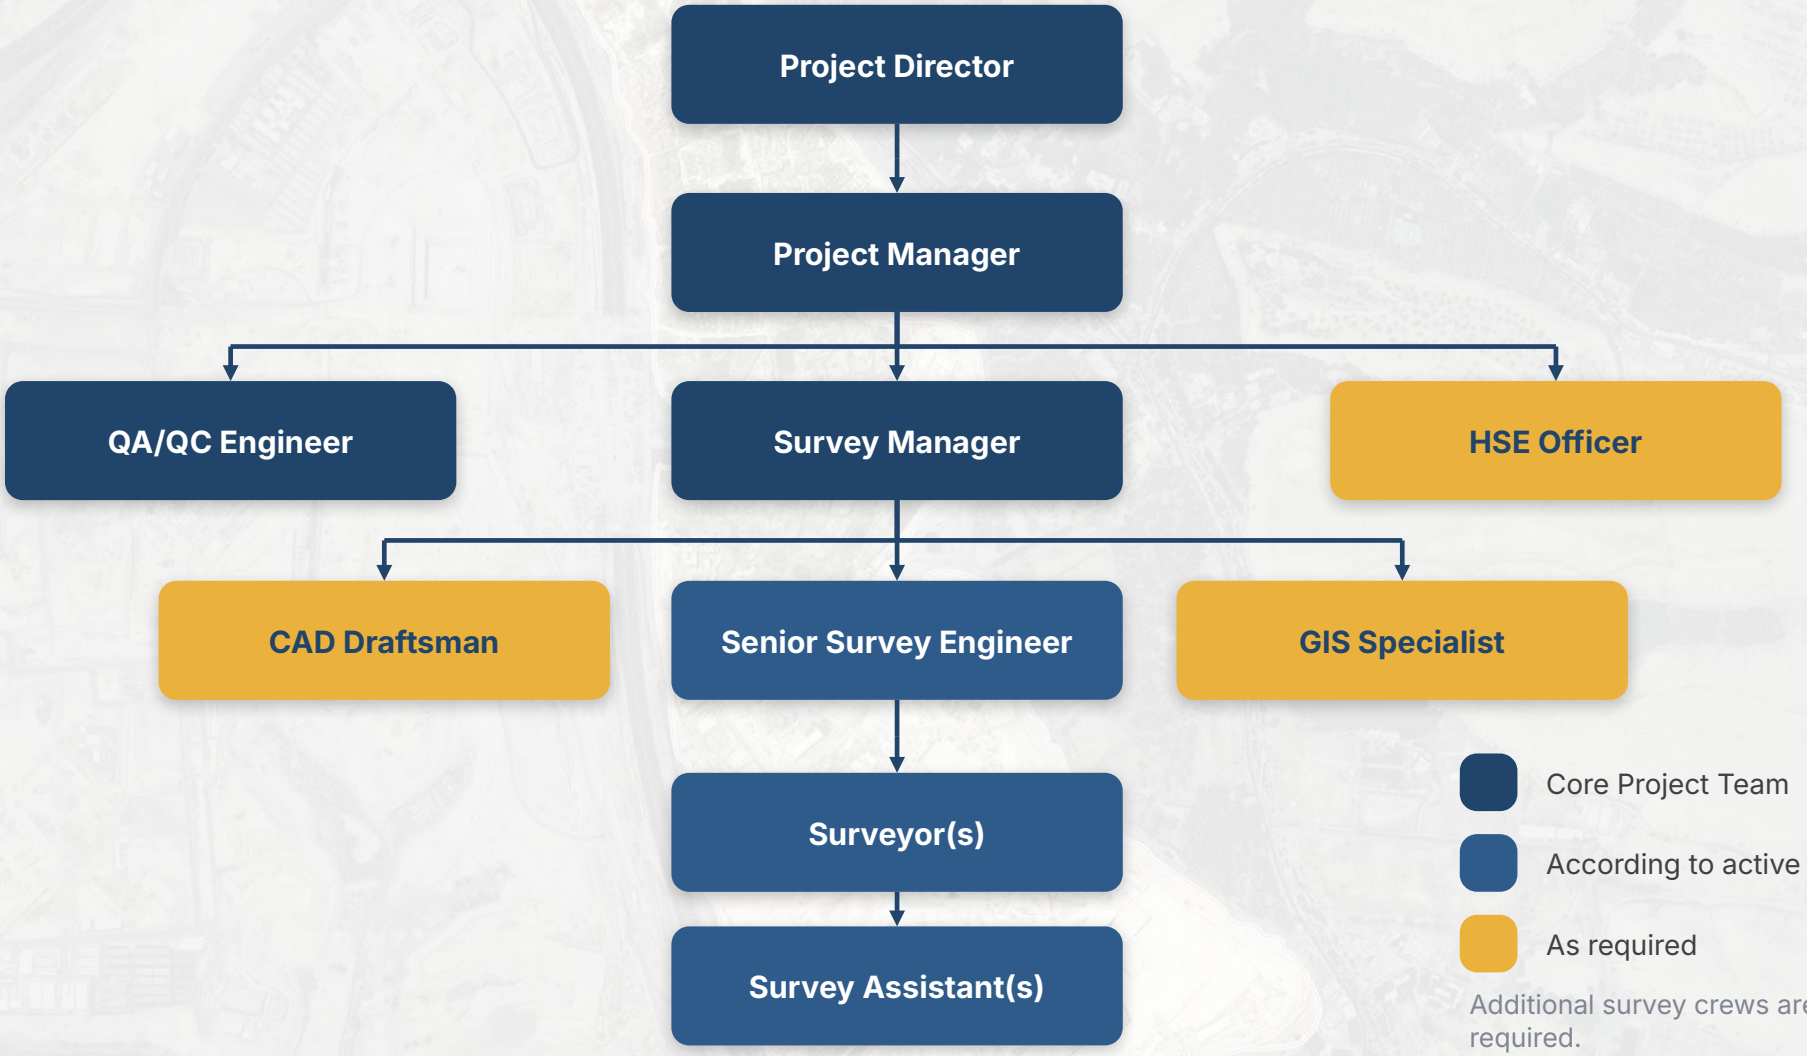
Project Director
Project Manager
QA/QC Engineer
Survey Manager
HSE Officer
CAD Draftsman
Senior Survey Engineer
GIS Specialist
Surveyor(s)
Survey Assistant(s)
Core Project Team
According to active Task Orders
As required
Additional survey crews are mobilized as required.

Typical Task Programme

Step 1: before work starts

Our proposal
Al Qotr
2 working days

Diriyah review
Diriyah team
2 working days

Commercial review
Diriyah
2 working days

6
working days to written authorisation

Step 2: delivery, duration agreed with Diriyah for each task

1 Plan and mobilize
- Scope and data review
- Resources
- Site access

Al Qotr | Diriyah

2 Survey
- Control verification
- Field survey
- Demarcation

Al Qotr

3 Prepare
- Processing
- Calculations
- Drawings

Al Qotr

4 QA/QC and submit
- Technical review
- QA/QC
- Submission

Al Qotr

5 Review
- Diriyah review
- Comments resolved
- Authority, if any

Diriyah | Al Qotr

6 Close-out
- Final submission
- Acceptance
- Records handover

Al Qotr | Diriyah

Duration of each step is agreed with Diriyah after the instruction

Roles and Responsibilities:

ALQOTR is fully committed to implementing this HSE Plan by establishing an agreed HSE Management System in order to:

- Execute all activities in compliance with KSA legal EHSMS framework, local requirements, international best practice, and contractual expectations.
- Provide leadership and guidance to middle management for the acceptance, maintenance and enforcement of the Loss Prevention Program.
- Achieve all occupational health, safety and environmental objectives set by Diriyah Company.
- Provide resources for training and monitoring the Loss Prevention Program.
- Maintain open lines of communication between employees, supervisors and management relative to the free exchange of safety suggestions and information.
- Protect the environment and utilize resources in the most efficient and effective manner.
- Promote and attend safety functions.
- Monitor the follow-up on recommendations made to improve performance and prevent accidents.

القطر
Alqotr



رؤية VISION 2030
المملكة العربية السعودية
KINGDOM OF SAUDI ARABIA

Contact us:

North Ring Road with Abu Bakr Al Siddiq Exit 6 Al Wadi Neighborhood, Riyadh

Jeddah, Sharifa District Saudi Business Center (607)

Khobar City - North Khobar Neighborhood - Prince Mohammed Bin Abdulaziz Road

Tel : 920029566
Tel : 0112403543

info@alqotr.sa
www.alqotr.sa
